



Elcho K-12 Facility Addition & Remodeling

Activity Report

July 30, 2018

OBJECTIVE:

ADDITION AND REMODELING OF EXISTING K-12 FACILITY

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

BILL FISHER

DISTRICT ADMINISTRATOR

715-275-3205

BFISHER@ELCHOSCHOOL.ORG

RECENT ACTIVITY:

- Finished installing lockers
- Continue installing bathroom partitions, grab bars and mirrors
- Completed demolition of south building
- Installed sunscreens
- Continue installing casework
- Continue installing tile
- Continue painting
- Continue installing food service equipment




CRITICAL UPCOMING EVENTS:

- Install instrument storage cabinets from Wenger - July 30
- Begin demolition of north building
- Southside Daycare Entrance - August 20
- Install stage life - August 27
- Start EIFS on south building - August 13

KEY DATES:

Upcoming Meetings:

- 07/31/2018 Progress Meeting
10:00 AM
- 08/07/2018 Progress Meeting
10:00 AM

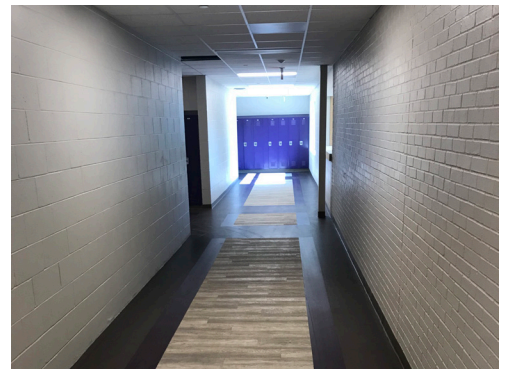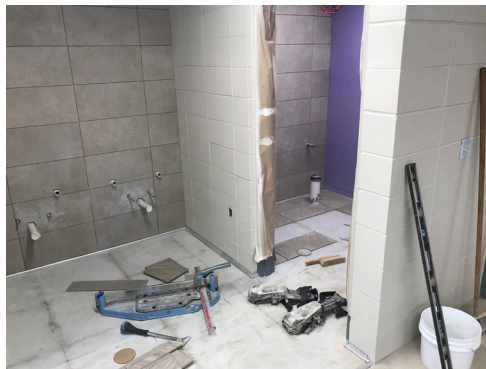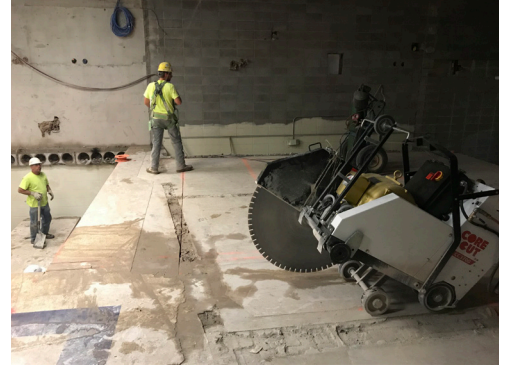

Construction: Phase I - New Construction
Construction: Phase II - New Construction

Occupancy

Construction: Phase III - Remodeling

Occupancy
Occupancy

April 2017 May 2017 June 2017 July 2017 Aug 2017 Sept 2017 Oct 2017 Nov 2017 Dec 2017 Jan 2018 Feb 2018 March 2018 April 2018 May 2018 June 2018 July 2018 Aug 2018 Sept 2018

↑
We are here
